

Traffic Signal Improvements at Foothill Blvd and Oakwood Ave


CIP 31-2107

ID	Task Name	Start	Finish	% Complete	2025												2026									
					Quarter	Nov	Dec	1st Quarter	Jan	Feb	Mar	2nd Quarter	Apr	May	Jun	3rd Quarter	Jul	Aug	Sep	4th Quarter	Oct	Nov	Dec	1st Quarter	Jan	Feb
1	READY TO LIST - ADVERTISEMENT AND AWARD PHASE	Thu 11/21/24	Thu 2/20/25	100%	[Timeline bar from Nov 2024 to Feb 2025]																					
2	Advertise for Bid	Thu 11/21/24	Tue 12/17/24	100%	[Timeline bar from Nov 2024 to Dec 2024]																					
3	Bid Opening	Wed 12/18/24	Wed 12/18/24	100%	[Timeline bar with diamond at 12/18]																					
4	Award of Construction Contract - City Council	Tue 1/21/25	Tue 1/21/25	100%	[Timeline bar with diamond at 1/21]																					
5	Notice of Award	Wed 1/22/25	Wed 1/22/25	100%	[Timeline bar with diamond at 1/22]																					
6	Execute Contract	Thu 1/23/25	Thu 2/20/25	100%	[Timeline bar from Jan 2025 to Feb 2025]																					
7	CONSTRUCTION PHASE	Mon 2/24/25	Tue 5/5/26	84%	[Timeline bar from Feb 2025 to May 2026]																					
8	1st NTP for Procurement Materials	Mon 2/24/25	Mon 2/24/25	100%	[Timeline bar with diamond at 2/24/25]																					
9	Procurement Materials	Mon 2/24/25	Mon 12/15/25	100%	[Timeline bar from Feb 2025 to Dec 2025]																					
10	2nd NTP for Construction	Tue 12/16/25	Tue 12/16/25	100%	[Timeline bar with diamond at 12/16/25]																					
11	Construction (55WD)	Mon 1/12/26	Thu 4/2/26	40%	[Timeline bar from Jan 2026 to Apr 2026]																					
12	Field Acceptance	Fri 4/3/26	Fri 4/17/26	0%	[Timeline bar from Apr 2026 to May 2026]																					
13	Notice of Completion (NOC) - City Council	Tue 5/5/26	Tue 5/5/26	0%	[Timeline bar with diamond at 5/5/26]																					
14	FINAL ACCOUNTING	Wed 5/6/26	Thu 6/4/26	0%	[Timeline bar from May 2026 to Jun 2026]																					

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

Mayor's Discovery Park Improvements

CIP 31-2213

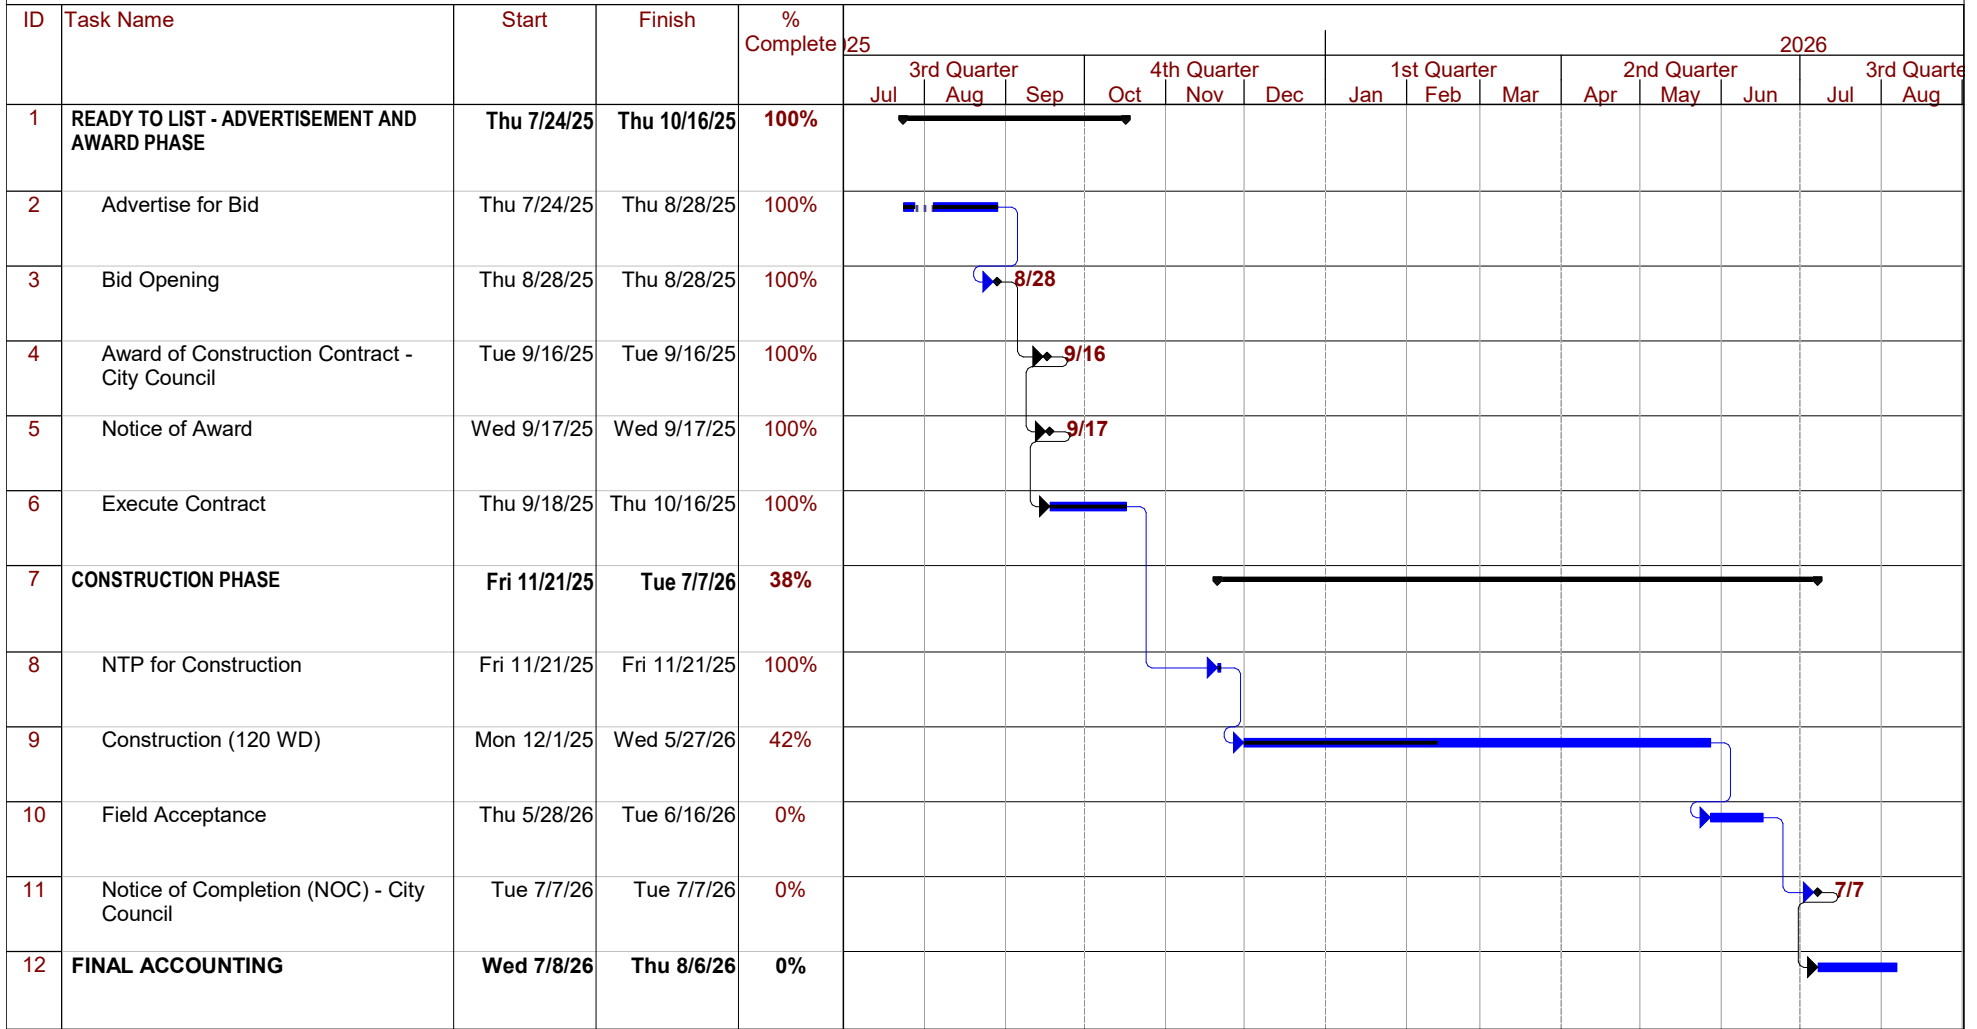

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

Traffic Signal Improvements at Foothill Blvd and Viro Rd


CIP 31-2404

ID	Task Name	Start	Finish	% Complete	2025												2026														
					4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter					
					Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
1	READY TO LIST - ADVERTISEMENT AND AWARD PHASE	Thu 10/31/24	Tue 1/21/25	100%	[Timeline bar from Oct to Jan]																										
2	Advertise for Bid	Thu 10/31/24	Tue 11/26/24	100%	[Timeline bar from Oct to Nov]																										
3	Bid Opening	Wed 11/27/24	Wed 11/27/24	100%	[Milestone diamond at 11/27]																										
4	Award of Construction Contract - City Council	Tue 12/17/24	Tue 12/17/24	100%	[Milestone diamond at 12/17]																										
5	Notice of Award	Wed 12/18/24	Wed 12/18/24	100%	[Milestone diamond at 12/18]																										
6	Execute Contract	Thu 12/19/24	Tue 1/21/25	100%	[Timeline bar from Dec to Jan]																										
7	CONSTRUCTION PHASE	Thu 1/23/25	Tue 5/19/26	87%	[Timeline bar from Jan to May]																										
8	1st NTP for Procurement Materials	Thu 1/23/25	Thu 1/23/25	100%	[Milestone diamond at 1/23]																										
9	Procurement Materials	Fri 1/24/25	Fri 11/14/25	100%	[Timeline bar from Jan to Nov]																										
10	2nd NTP for Construction	Thu 12/11/25	Thu 12/11/25	100%	[Milestone diamond at 12/11]																										
11	Construction (55 WD)	Mon 1/12/26	Thu 4/2/26	60%	[Timeline bar from Jan to Apr]																										
12	Field Acceptance	Fri 4/3/26	Tue 4/21/26	0%	[Timeline bar from Apr to Apr]																										
13	Notice of Completion (NOC) - City Council	Tue 5/19/26	Tue 5/19/26	0%	[Milestone diamond at 5/19]																										
14	FINAL ACCOUNTING	Wed 5/20/26	Wed 6/17/26	0%	[Timeline bar from May to Jun]																										

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

Traffic Signal at 200 Foothill Blvd Mid- Block Pedestrian Crossing

CIP 7000-2423d

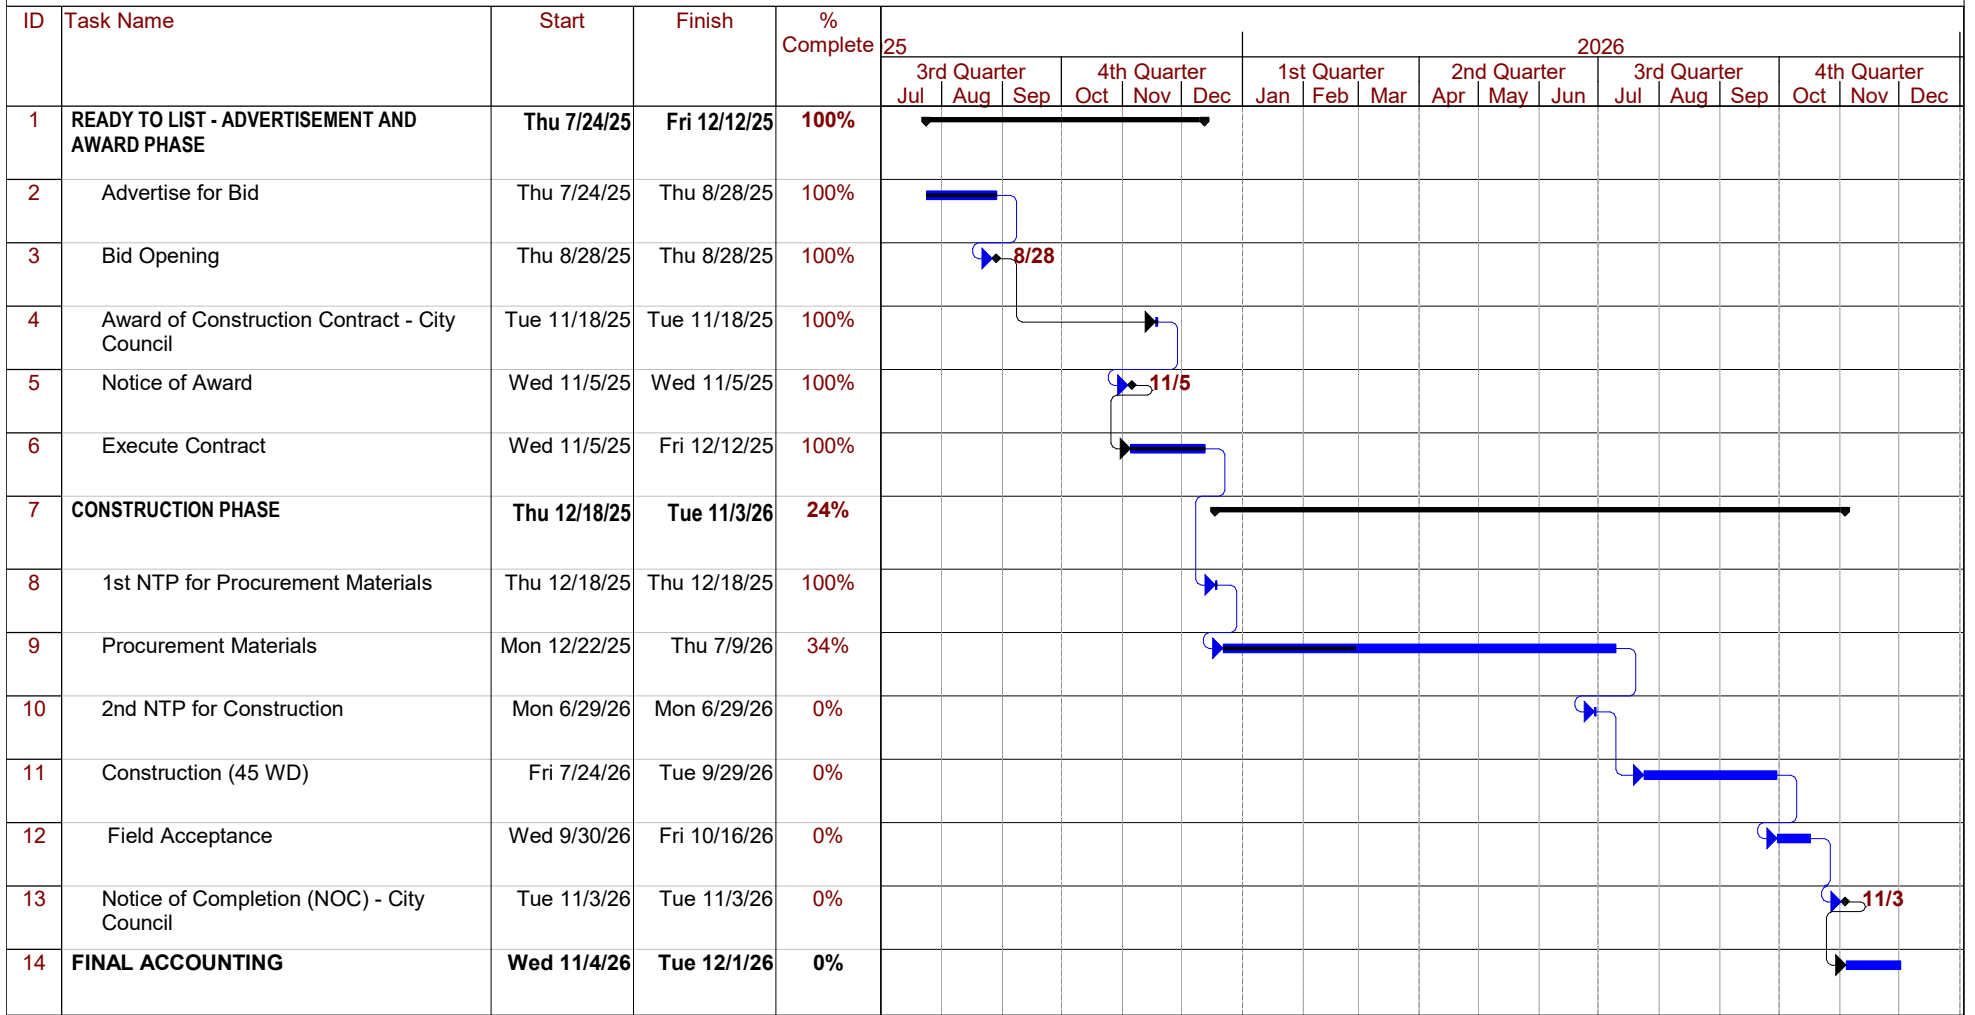

Task		Inactive Milestone		Finish-only	
Split		Inactive Summary		External Tasks	
Milestone		Manual Task		External Milestone	
Summary		Duration-only		Progress	
Project Summary		Manual Summary Rollup		Deadline	
External Tasks		Manual Summary			
External Milestone		Start-only			

